

BuildFlow

Product Feature Roadmap

BuildFlow will be an offline-first construction operations platform for small and mid-sized contractors. This document sets out which features will ship in the MVP and which are planned for later releases. The MVP is exactly the Po set of the PRD — nothing heavier. Timing is given in weeks from the start of the build, because each release is gated by its exit criteria rather than by a calendar.

11

MVP feature areas
every one a PRD P0

16

weeks to the pilot
build 1–12, pilot 13–16

13

excluded from the MVP
each with where it lands

3


later releases
one paid, two candidate

Contents

Roadmap at a glance	02
MVP scope — on site, works offline	03
MVP scope — office, money and compliance	04
MVP release gate and pilot metrics	05
Deliberately out of the MVP	06
Release 2 — Paid MVP	07
Release 3 — Operations and money	08
Release 4 — Demand-gated expansion	09
How the next item is chosen	10

Roadmap at a Glance


One release is the MVP, and it runs for sixteen weeks. Everything after it is a candidate: Release 2 is committed because the product must become billable, and Releases 3 and 4 are built only if customers ask.

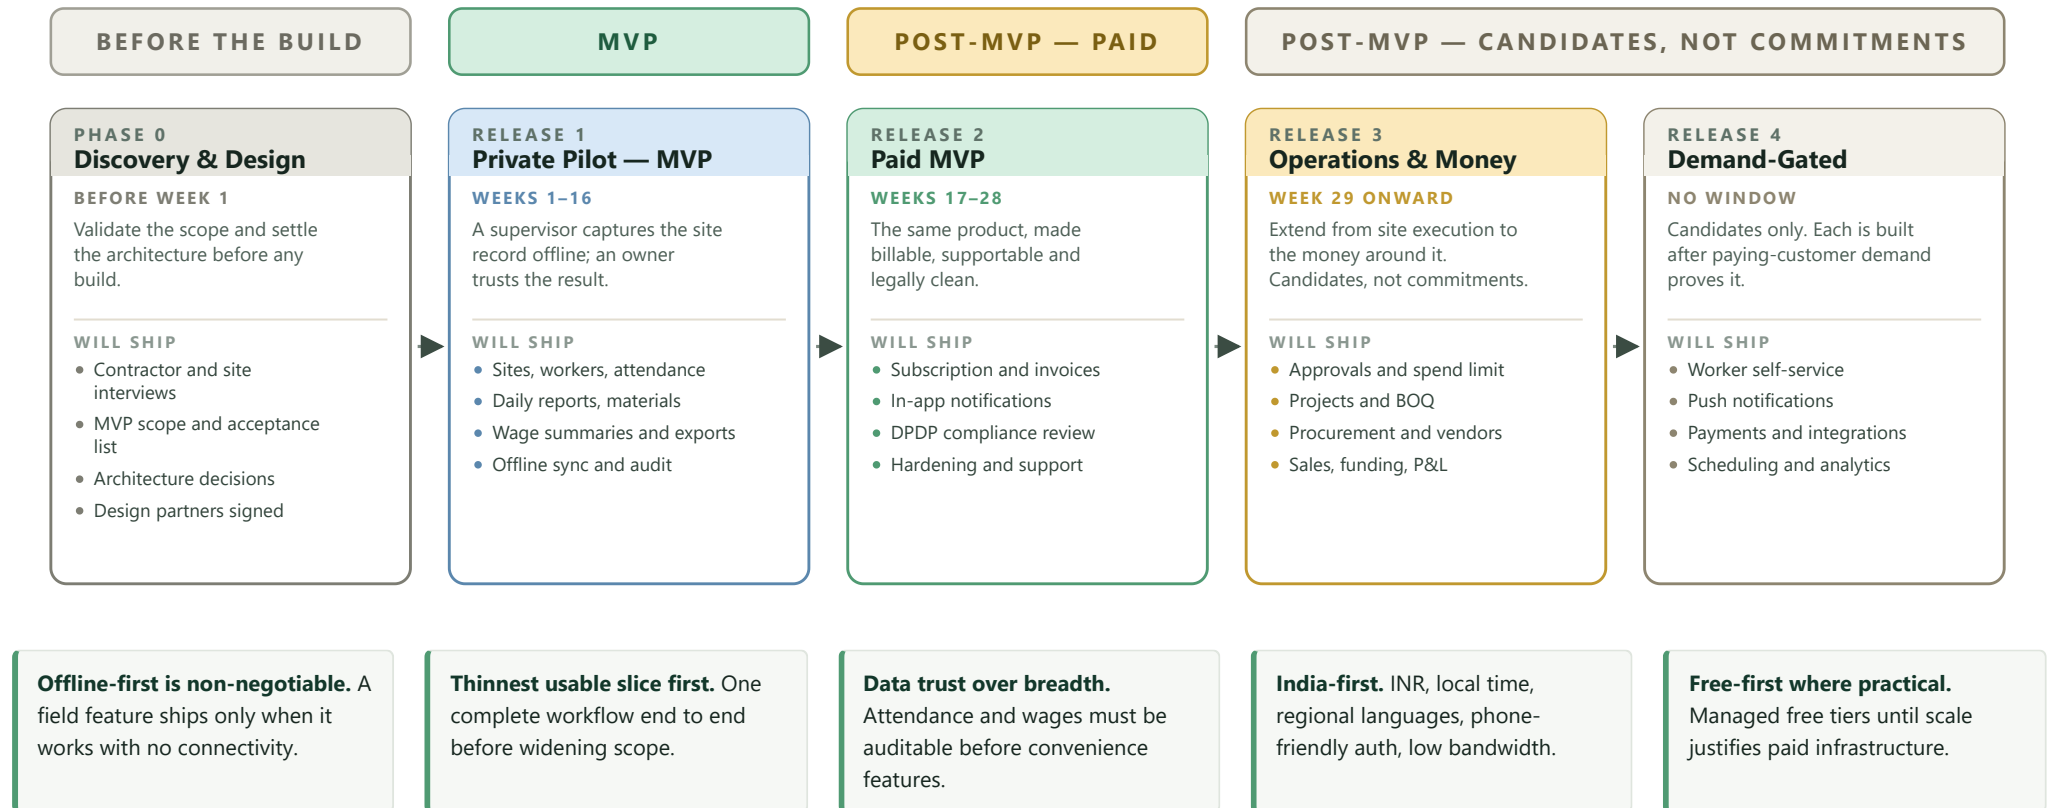

Weeks are counted from the start of the build, not from a calendar date, because every release is gated by its exit criteria. Release 1 will not be called complete until the core workflows run fully offline and sync without data loss, 3–5 pilot contractors have used the product for at least two weeks, the north-star metric is trending as expected, and no critical defect remains. Release 2 will not start before that, and Release 3 is not confirmed until the Release 2 gate is met.

MVP Scope — On Site, Works Offline

Weeks 1–16. These areas will ship in the private-pilot release. Every one is a PO in the PRD, and every one will work with no connectivity.

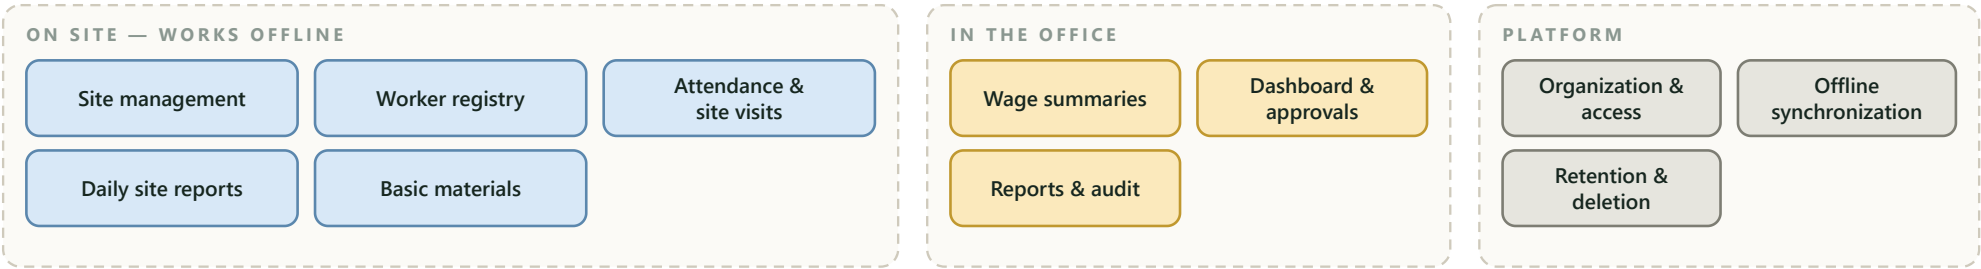

MVP area	Features that will ship
Site management CUJ-1	Create and edit sites · address and map pin · geofence radius · supervisor and project-manager assignment · status of planned, active, paused, completed or archived
Worker registry CUJ-1	Worker code, name, phone, trade and labour group · assignment to sites · daily or monthly pay type · effective-dated wage rates · import through CSV or XLSX
Attendance and site visits CUJ-2	Session-based check-in: timestamp, approximate location, accuracy and geofence result are captured once, on the session · marking is then one tap per worker for present, absent or overtime · half-day, leave, holiday, exact overtime hours and per-worker notes sit behind a per-row menu · running totals stay visible · an outside-geofence attempt needs a reason or manager review · corrections keep both original and proposed values
Daily site reports CUJ-3	Site, date and reporting supervisor · headcount by trade · work completed · progress estimate or completed quantity · materials received and used · blockers and issues · safety incident flag · next-day plan · optional photos, which will never block a submission
Basic materials CUJ-3	Materials defined per site · unit and low-stock threshold · opening balance, receipt, usage and adjustment · estimated balance · warning on a low or negative balance · a mandatory reason on every adjustment
Offline synchronization CUJ-2, 3	Check-in and check-out, attendance, daily reports and basic material transactions will all work with no connectivity · the app will show pending, syncing, synced, failed, conflict and rejected · it will never show “submitted” before the server confirms · a repeated push will not create a duplicate record

MVP Scope — Office, Money and Compliance

Weeks 1–16, the same release. These are what an owner, project manager or accountant uses to review the record the field captured. Each is a PRD Po; nothing heavier than a Po is in the MVP.

MVP area	Features that will ship
Organization and access CUJ-1	Create an organization · set timezone, currency and default language · invite users · assign roles · assign supervisors and managers to sites · enforce organization-level and site-level access
Wage summaries CUJ-4	Daily and monthly rates · approved attendance only · payable units · overtime and authorised adjustments · the calculation inputs shown, not just the result · weekly or monthly periods · lock and reopen through authorised actions · payment status · export
Dashboard and approvals CUJ-5	Active sites · missing attendance · missing daily reports · pending approvals · geofence exceptions · attendance corrections · estimated wage totals · material alerts · critical blockers · safety flags · latest site updates
Reports and audit CUJ-5, 6	CSV and Excel exports for attendance, wage summary, daily reports, material transactions and balances, and site activity and exceptions, with exported figures always matching what the app shows · a full export of a customer's own data on exit · an audit trail of user and role changes, site and geofence changes, attendance corrections, wage-rate changes, material adjustments, approvals and rejections, and wage-period lock and reopen events
Data retention and deletion CUJ-6	Removing a user or a worker will never delete their history, and old records will still show who created them · a finished site can be archived and becomes read-only · deactivating a user, worker or site will remove access, not history · attendance and wage records retained a minimum of three years, with a worker inside that floor anonymised rather than deleted

Two limits are deliberate and will hold through the MVP. BuildFlow will not transfer wages and will not give statutory payroll advice; it will produce the summary an accountant pays from. And workers will have no login of their own — the contractor enters and owns the worker record.

MVP Release Gate and Pilot Metrics

The pilot runs in weeks 13–16, and starts only when every gate below is met. The compliance gate blocks entering real worker data, not just launch.

Gates that must be met

Gate	What must be true
Access and isolation	An admin can create an organization, users, sites and workers. A supervisor sees only assigned sites. Row Level Security and role permissions pass positive and negative tests.
Field reliability	Check-in and check-out capture location explicitly. Attendance saves offline and synchronizes later. Duplicate sync retries create no duplicate records. Sync failures are visible and recoverable.
Speed of the common path	A normal daily report is completed in five minutes or less. Photos are optional and never block submission.
Data trust	Wage summaries use approved attendance only. Payroll periods lock and reopen by authorised roles. CSV and XLSX exports match in-app values. Critical changes appear in the audit log.
Language	English is complete. Hindi and Marathi translation support is enabled technically, even though the translations themselves are later scope.
Compliance blocks real worker data	A privacy notice and worker-data consent step are shown before worker data entry. The retention and deletion policy is implemented, not only documented. A DPA and Terms of Service are executed with each pilot customer.
Operational readiness	A database backup has been restored at least once as a rehearsal, before the first customer's data is entered. Pilot users work without direct developer assistance after onboarding.

Pilot success metrics

Metric	Target
Sites with same-day attendance and report	80% of active sites, five days a week
Daily report completion time	Five minutes or less for a normal report
Supervisor activity	60% or more still active after two weeks
Offline sync success	99% or more of queued records eventually sync
Wage preparation time	50% faster than the customer's current process
Paid continuation	At least 3 of 5 pilot customers

North-star metric: active sites with verified attendance and a completed daily report on the same working day. Every other metric supports it.

Pilot shape: 3–5 contractor companies, 5–10 active sites, human-assisted setup and data import, with a weekly adoption and reliability review and deliberate offline test days.

Deliberately Out of the MVP

These will not be built for the pilot. Each is listed with where it is planned, so an exclusion reads as a scheduling decision rather than a silent gap.

Excluded from the MVP	Planned in	Why it waits
Worker self-service login	Release 4	Only if workers repeatedly ask supervisors for their own record.
UPI wage payments	Release 4	Moving money brings regulatory scope the pilot does not need.
WhatsApp or SMS delivery	Not planned	Pilot invites will be sent by hand as a copied link.
Purchase orders and vendor management	Release 3 <i>candidate</i>	Moved out of this list on purpose once owner spend became part of the product.
Stock transfer between sites	Not planned	No pilot demand recorded.
Full expense management	Release 3 <i>candidate</i>	Would arrive as site spend, under the owner threshold.
Gantt charts and advanced scheduling	Release 4	Only if customers plan labour more than a day ahead.
BIM or design tools	Not planned	Outside the operations problem BuildFlow solves.
Accounting, GST or statutory payroll integrations	Release 3 and 4	Accounting-ready exports in Release 3; a Tally or GST integration only on demand.
AI summaries	Not planned	Adds no trust to a record an owner must rely on.
Continuous employee location tracking	Not planned	Location will be captured once per session, on an explicit action, and never continuously.
Social or photo-sharing features	Not planned	Not an operations need.
Procurement marketplace	Not planned	A different business, not a later feature.

One exclusion has been revisited on purpose. Purchase orders and vendor management were excluded when the product was scoped as construction execution only. Once the owner's money became part of the thinking, a committed spend the owner never sees looked like a gap worth closing, so they become a Release 3 candidate — not a commitment. The original exclusion is kept on the record rather than quietly deleted.

Release 2 — Paid MVP


Weeks 17–28. Release 2 adds no new field capability. It makes what has already shipped billable, supportable and legally clean.

Workstream	What will ship
Billing and plans	A per-organization monthly subscription billed in INR, tiered by active-site count: a small band for 2–5 sites, a mid band for 6–12, a top band for 13–20. Invoice generation. No per-export or per-photo charges, so pricing stays as simple as the product.
In-app notifications	One list per user of what is waiting for them, so an approval is not missed because nobody opened the dashboard.
Statutory exports	A muster-roll export per site and period on the Form XIV pattern, for BOCW Act recordkeeping, and a statutory wage register export for Payment of Wages Act recordkeeping. Held back from the MVP because no PRD P0 requires either, and the format needs a real customer's auditor to confirm it.
DPDP compliance review	Appoint a grievance officer. Finalise the breach-notification runbook for 72-hour reporting to the Data Protection Board. Obtain counsel sign-off on the retention-versus-erasure exception the MVP relies on.
Hardening and scale	Performance tuning, backup and recovery verification, and rate limiting.
Support and onboarding	Admin training, guided setup and help documentation. Materials enabled selectively rather than for everyone at once.
Refined reporting	Export formatting, scheduled exports and advanced filters.
Security review	A penetration-test pass, and hardening of the consent and location audit.

Release 2 will be complete when at least one design partner converts to a paying customer, the billed cloud usage is covered by revenue, and the support workload is sustainable for a small team.

Release 3 — Operations and Money

Release 3 is a candidate list, not committed scope. Nothing here is decided before a contractor has used the product. Each group is scoped far enough to estimate, and each will be confirmed or dropped at the Release 2 gate.

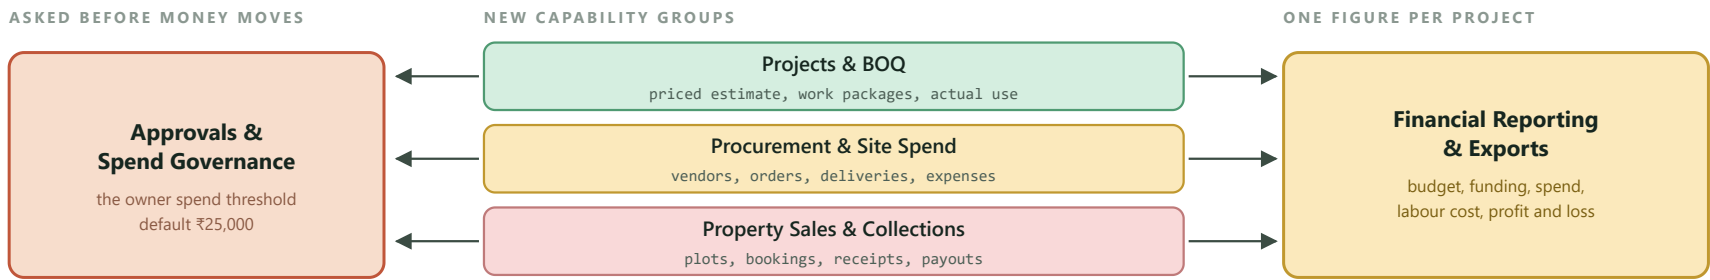

Capability group	What it will add	Depends on
Approvals and spend governance	One request-and-decide path shared by every module that spends money or deletes something. An owner spend threshold, default ₹25,000, with a per-action override. At or below the line, approval is automatic and no request is raised at all; above it, only the owner may decide. Only the owner may move the line.	Identity and access
Projects and BOQ	Projects sitting above sites. A priced bill of quantities held by version, work packages, and actual use recorded against the estimate so an owner can see estimate against actual.	Sites, Materials
Procurement and site spend	Vendors, purchase orders with lines, full or partial delivery confirmation, site expenses captured in the field, and vendor payments. A purchase-order total will be summed from its lines and never accepted from the caller. Confirming a delivery will post one stock movement per delivered line.	Approvals, Materials
Property sales and collections	Plots, bookings, booking receipts, brokers and broker payouts. A plot will hold only one live booking at a time, and a commission will not exceed what the booking owes or be paid on a cancelled sale.	Approvals
Financial reporting and exports	Project budget and funding, project spend, labour cost attributed to projects in proportion to the approved attendance behind each wage line, profit and loss, and accounting-ready exports.	Procurement, Payroll, Sales

Release 4 — Demand-Gated Expansion

No window. Release 4 items are candidates, not commitments. Each will be adopted only after paying customers show real demand, and each is listed with the signal that would justify building it.

Candidate	What it would add	The signal that would justify it
Worker self-service app	Workers view their own attendance, wages and payslips.	Workers repeatedly asking supervisors for their own record.
Push notifications	Approvals, exceptions and reminders delivered to the device.	In-app notifications proving too slow for time-critical approvals.
Advanced material management	Suppliers and stock levels beyond the per-site ledger.	Customers moving stock between sites.
Payments and wage disbursement	Paying wages from inside the product, including UPI.	Customers asking to pay from the product, and the regulatory work that follows.
Payroll and accounting integrations	Tally and GST invoicing.	Accountants re-keying BuildFlow exports into Tally.
Multi-language beyond English	Hindi and regional languages fully translated.	Supervisors unable to work in English.
Shift planning and scheduling	Rosters and schedules set ahead of the day.	Customers planning labour more than a day ahead.
Analytics dashboards	Productivity and material wastage.	Owners asking questions the exports cannot answer.

Anything that does not strengthen the MVP promise in an upcoming release will be deferred. The promise is that a supervisor can capture the essential site record even without internet, and an owner can trust the resulting data enough to make a decision.

How the Next Item Is Chosen

Priority will be decided by score rather than by argument, and every release is gated by its own exit criteria. The risks below are the ones that would change the plan.

Prioritisation

Criterion	Weight	The question it answers
Value to core user	High	Does it save field or owner time?
Data trust impact	High	Does it strengthen auditability or accuracy?
Build cost	Medium	Effort given the architecture already chosen.
Pilot demand signal	Medium	Have customers explicitly asked for it?
Strategic fit	Low	Does it fit the long-term platform direction?

Review cadence

- 1. Weekly: an engineering demo and sync.
- 2. Bi-weekly: a product decision review with design partners.
- 3. Per release: an exit-criteria review before committing to the next one.
- 4. Continuous: metric dashboards updated from product analytics and usage data.

Risks that would change the plan

Risk	Mitigation
Offline sync data loss or conflict	Outbox pattern, conflict resolution, sync test suite.
Low pilot adoption	Design partners co-create scope; thin vertical slices; frequent feedback.
Location privacy pushback	Consent-based, action-triggered location capture only.
Free-tier scaling limits	A planned upgrade path to paid tiers.
Small-team bandwidth	A modular monolith and free-first managed services.
Retention law against labour-law recordkeeping	A documented retention exception, plus counsel review before paid launch.
Worker consent friction	A one-time consent step at onboarding, with BuildFlow supplying the notice template.
